

Work Order ID 150690

Monday, August 29, 2016 3:01:34 PM

150690

Page 1

Item ID: D119-796-251

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: AFT Crosstube Installation with Step (no hardware)

Start Date: 8/17/2016 Start Qty: 1.00 ***1***

Cust Item ID:

Required Date: 9/13/2016 Req'd Qty: 1.00 ***1***

Customer:

Reference:

Approvals: Process Plan: DAS Date: **AUG 30 2016** Tooling: _____ Date: _____
QC: 21 Date: _____ SPC (Y/N): _____ Date: _____
9-89

Run Start ***NR1***Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
----------	--------------

D119-796-251	D
--------------	---

110	Document Control	0.00
-----	------------------	------

110

DC

Memo

0.00

Doc.Control -USB or Paperwork

Photocopy bluefile and create labels as per PPP D119-796-251 chg 002

120	Pick Kit	0.00
-----	----------	------

120

Packaging

Memo

0.00

Packaging

1

130	Crosstubes	0.00
-----	------------	------

130

Crosstubes

Memo

0.08

Crosstubes

1- Install step and clamp with the proper position per dwg D119-796-251

Torque all clamps to 50 IN-LBS max.

1

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval	
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐			
Design ☐	☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐			
Doc/Data ☐	☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐			
Equip/Tooling ☐	☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐			
Handling/Pre ☐	☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐			
Material ☐	☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐			
Internal Transport ☐	☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐			
Tribal Knowledge ☐	☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐			
LOA ☐	☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐			
Substation ☐	☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐			
Past Expiry Date ☐	☐	Manufacturing Process ☐	OTHER : _____						
Misidentified ☐	☐	Past Due ☐							

Monday, August 29, 2016 3:01:34 PM

Page 2

M 16-11-28

WORK ORDER NON-CONFORMANCE / UPDATE



QA Closed:

Date:

Work Order update only

☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Cross tube ☐ Water Jet ☐ Engineering ☐ Machining ☐ Small Fab ☐ Prod. Eng. Coord. ☐ Quality ☐ Thermoforming ☐ Finishing ☐ Rec/Store/Packaging ☐ Other ☐ Large Fab ☐ Composite ☐ Supplier ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause Environment ☐ No Re-verification ☐ Design ☐ Operator ☐ Doc/Data ☐ Offset/Setup ☐ Equip/Tooling ☐ Supplier ☐ Handling/Pre ☐ Training ☐ Material ☐ Use for Testing ☐ Internal Transport ☐ Poor Information ☐ Tribal Knowledge ☐ Rushing ☐ LOA ☐ Product Improvement ☐ Substation ☐ Process Improvement ☐ Past Expiry Date ☐ Manufacturing Process ☐ Misidentified ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Temperature/Cure ☐ Power Loss/Surge ☐ Positioned Wrong ☐ Bending ☐ Set-up ☐ Folio/Program ☐ Outside Dimensions ☐ Centre Not Concentric ☐ BOM/Route ☐ Grain ☐ Over/Under tolerance ☐ Cracks ☐ Broken/Damage/Defect ☐ Weld ☐ Part Incorrect ☐ Crimp/Kink/Ripple/Wave ☐ Inspection Incomplete/Unqualified ☐ Wrong Stock Pulled ☐ Part Lost/Missing ☐ Cuffs ☐ Contamination ☐ Out of Sequence ☐ Part Moved ☐ Crushing ☐ Countersink ☐ Off-set ☐ Drawing ☐ Heat Treat ☐ Cut Too Short ☐ Mislabeled ☐ Finish ☐ Wave/Twist in Tube ☐ Instructions Incomplete/Unclear ☐ Fit/Function ☐ Misread ☐ Marks/Chatter ☐ Drill Holes ☐ Misaligned/off center ☐ Turning Sequence ☐							
OTHER :									

Picklist Print

Monday, August 29, 2016 3:01:33 PM

Page 1

Work Order ID: 150690

150690

Parent Item: D119-796-251

D119-796-251

Parent Item Name: AFT Crosstube Installation with Step (no hardware)

Start Date: 8/17/2016

Required Date: 9/13/2016

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP REV:A 14.09.09 NEW ISSUE DD VERF:JLM IPP REV:B
14.10.15 AS PER REV.A DD VERF:JLM IPP REV:C 14.11.19
AS PER REV.C DD VERF:JLM IPP REV:D 14.12.09 AS PER
REV.PC6 DD VERF:JLM IPP REV:E 15.02.11 AS PER REV D
JLM VERF:DD

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	-------------	--------------	---------------	----------------	--------

D119-796-241

Manufactured No

Each 1.0000

1

D119-796-241

150597

**

1

AFT Crosstube Installation without Step (no hardware)

MA 16-11-16

Location

Loc Qty

Loc Code

FG

1

146580

1

D5123-3

Manufactured No

Each 88.0000

4

D5123-3

Clamp Cushion

**

4

MA 16-11-16

Location

Loc Qty

Loc Code

LG054

12

147939

12

LG055

76

146879

16

148184

24

149113

36

D5149-043

Manufactured No

Each 8.0000

2

D5149-043

Aft Step Base Assembly

**

2

MA 16-11-27

Location

Loc Qty

Loc Code

LG055

8

142738

6

149108

2

149667

2

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width:100%; border: none;"> <tr> <td style="width:12.5%;">Skid-tube ☐</td> <td style="width:12.5%;">Cross tube ☐</td> <td style="width:12.5%;">Water Jet ☐</td> <td style="width:12.5%;">Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																						
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																						
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																						
Large Fab ☐	Composite ☐	Supplier ☐																							
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval																		
Description Work Order Deviation				Disposition																					
Root Cause		FAULT CATEGORY																							
Environment ☐		No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐																			
Design ☐		Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐																			
Doc/Data ☐		Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐																			
Equip/Tooling ☐		Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐																			
Handling/Pre ☐		Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐																			
Material ☐		Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐																			
Internal Transport ☐		Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐																			
Tribal Knowledge ☐		Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐																			
LOA ☐		Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐																			
Substation ☐		Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐																			
Past Expiry Date ☐		Manufacturing Process ☐	OTHER :																						
Misidentified ☐		Past Due ☐																							

Picklist Print

Monday, August 29, 2016 3:01:33 PM

Page 2

Work Order ID: 150690

150690

Parent Item: D119-796-251

D119-796-251

Parent Item Name: AFT Crosstube Installation with Step (no hardware)

Start Date: 8/17/2016

Required Date: 9/13/2016

Start Qty: 1.00

Required Qty: 1.00

MS21920-25

Purchased

No

Each

5.0000

4

MS21920-25

Clamp

4

NAF
16.11.16

Location

Loc Qty

Loc Code

FG

4

120920

2

m134987

2

LG050

1

120920

0

m135444

1

135787 - 4

WORK ORDER NON-CONFORMANCE / UPDATE


QA Closed:

Date:


Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By 		
							Lead hand / Supervisor Approval Verification 		
							QC / QA Coordinator Approval 		
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER :							
Misidentified ☐	Past Due ☐								

ITEM	QTY	P/N	DESCRIPTION
	X	D119-796-251	XTUBE ASSY (AW119 MKII AFT)
1	1	D119-796-241	XTUBE ASSY (AW119 MKII AFT)
2	4	D5123-3	CUSHION
3	2	D5149-043	AFT STEP ASSY
4	4	MS21920-25	CLAMP

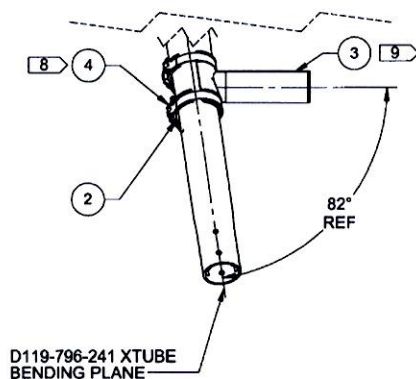

SECTION A-A

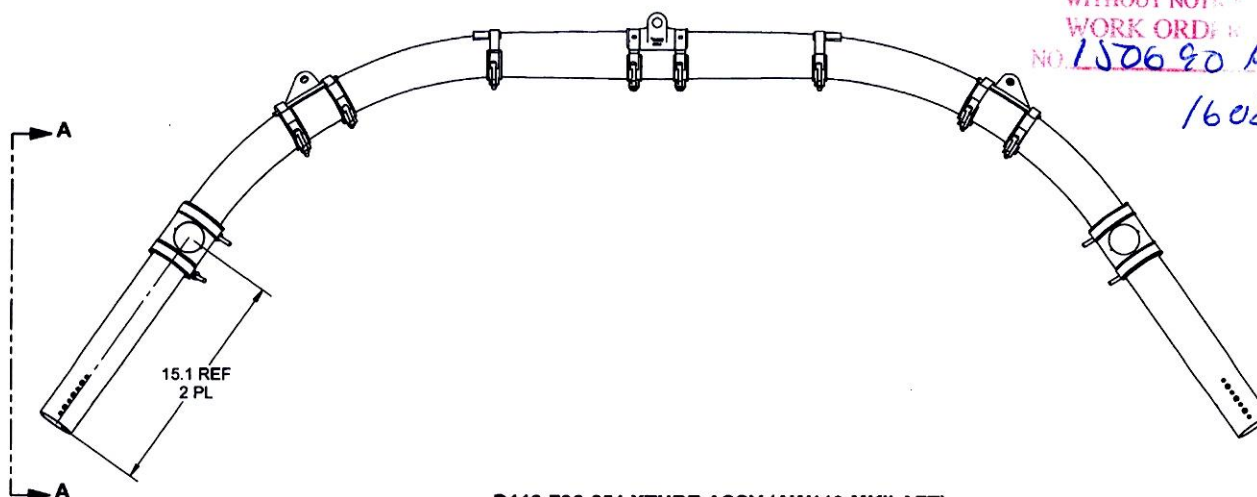

D119-796-251 XTUBE ASSY (AW119 MKII AFT)

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY PER DART QSI 044 METHOD 6.5
- 7) WEIGHT: 29.9 lbs
- 8) TORQUE MS21920-25 CLAMPS TO 50 IN-LBS MAX
- 9) LOCATE STEP USING POST FITTING ON CROSSTUBE

RELEASED

2015 FEB 09

ECN 15-516

D	D5123-3 WAS D5123-9, MS21920-25 WAS -26. ADDED SECTION A-A	AP	15.01.19
C	RE-DESIGN STEP INSTALLATION	DB	14.11.24
B	D2274 RADIUS BLOCK WAS D5153-1, AN4C12A WAS AN4C10A	AP	14.10.04
A	NEW ISSUE	AP	14.09.03
REV.	DESCRIPTION	BY	DATE
DESIGN	AP		
DRAWN	AP		
CHECKED	DB	DART AEROSPACE LTD	REV. D
MFG. APPR.	DD	HAWKESBURY, ONTARIO, CANADA	
APPROVED	HS	D119-796-251	SHEET 1 OF 1
DE APPR.	DS	XTUBE ASSY (AW119 MKII AFT)	SCALE
DATE	15.01.19		NTS

APPROVED

COPYRIGHT © 2014 BY DART AEROSPACE LTD
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER NO. 150690 MWS
160830
